





URBANDALE
ELEMENTARY
SCHOOL

- Construction Timeline
- Demolition
- Traffic/ Sidewalk Impacts
- Site Layout
- Equipment
- Safety
- Hours of Operation




ID	Task Name	Duration	Start	Finish	2020												2021																		
					May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul				
1																																			
2	Site Fencing	1 wk	Mon 7/8/19	Fri 7/12/19																															
3	Mobilization	1 wk	Mon 7/8/19	Fri 7/12/19																															
4	Demolition	8 wks	Mon 7/15/19	Fri 9/6/19																															
5	Grading	4 wks	Mon 9/9/19	Fri 10/4/19																															
6	Building enclosure	54 wks	Mon 10/7/19	Fri 10/16/20																															
7	Interior Work	65 wks	Mon 1/20/20	Fri 4/16/21																															
8	Substantial completion	1 wk	Mon 4/19/21	Fri 4/23/21																															
9	Demobilization	1 wk	Mon 4/26/21	Fri 4/30/21																															

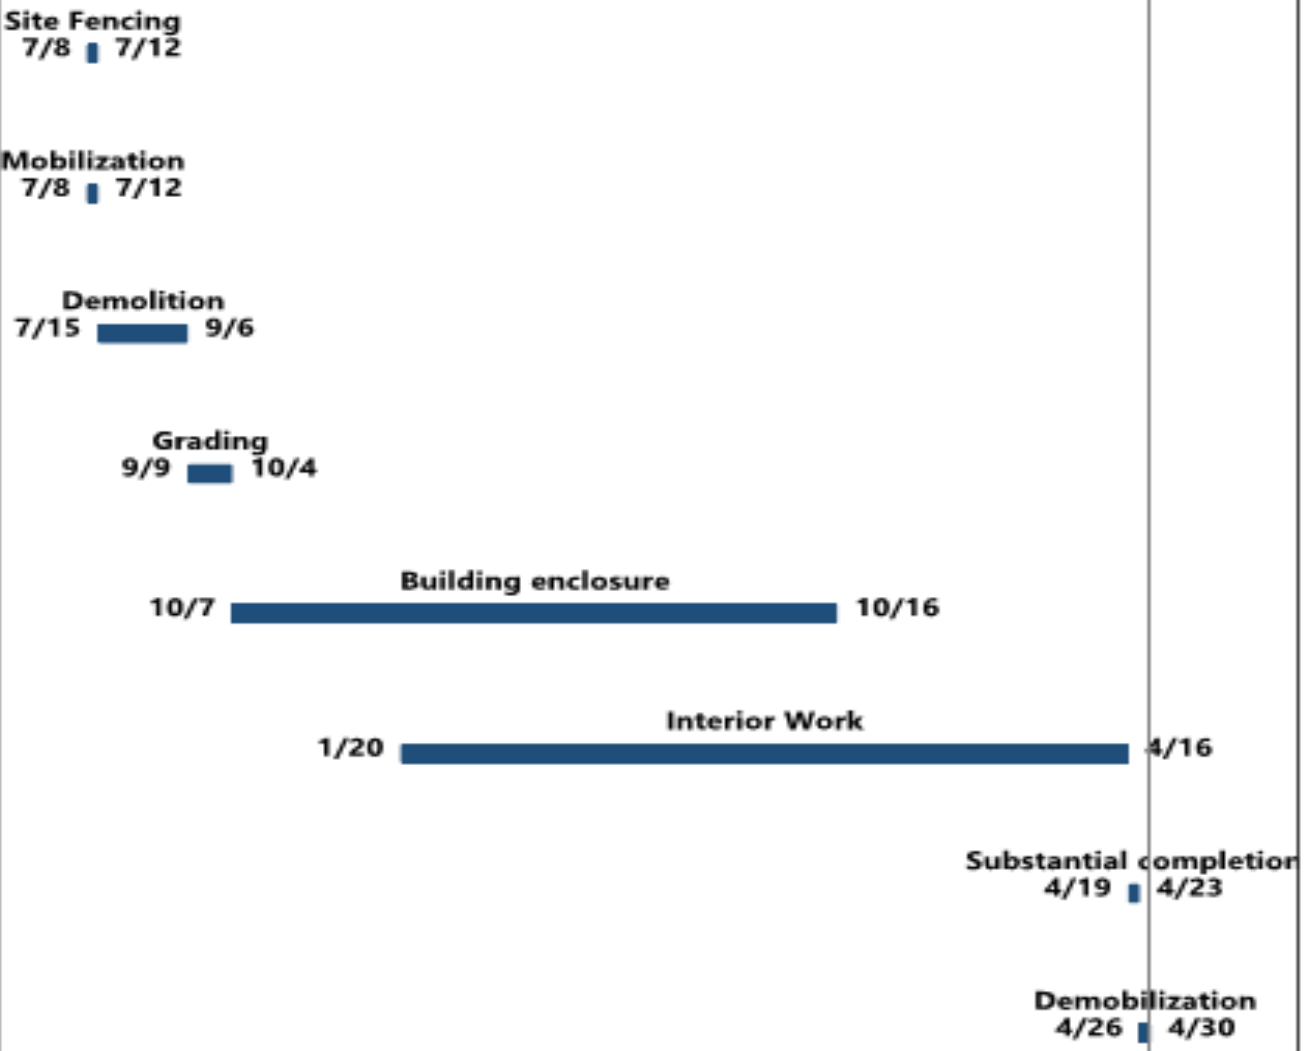

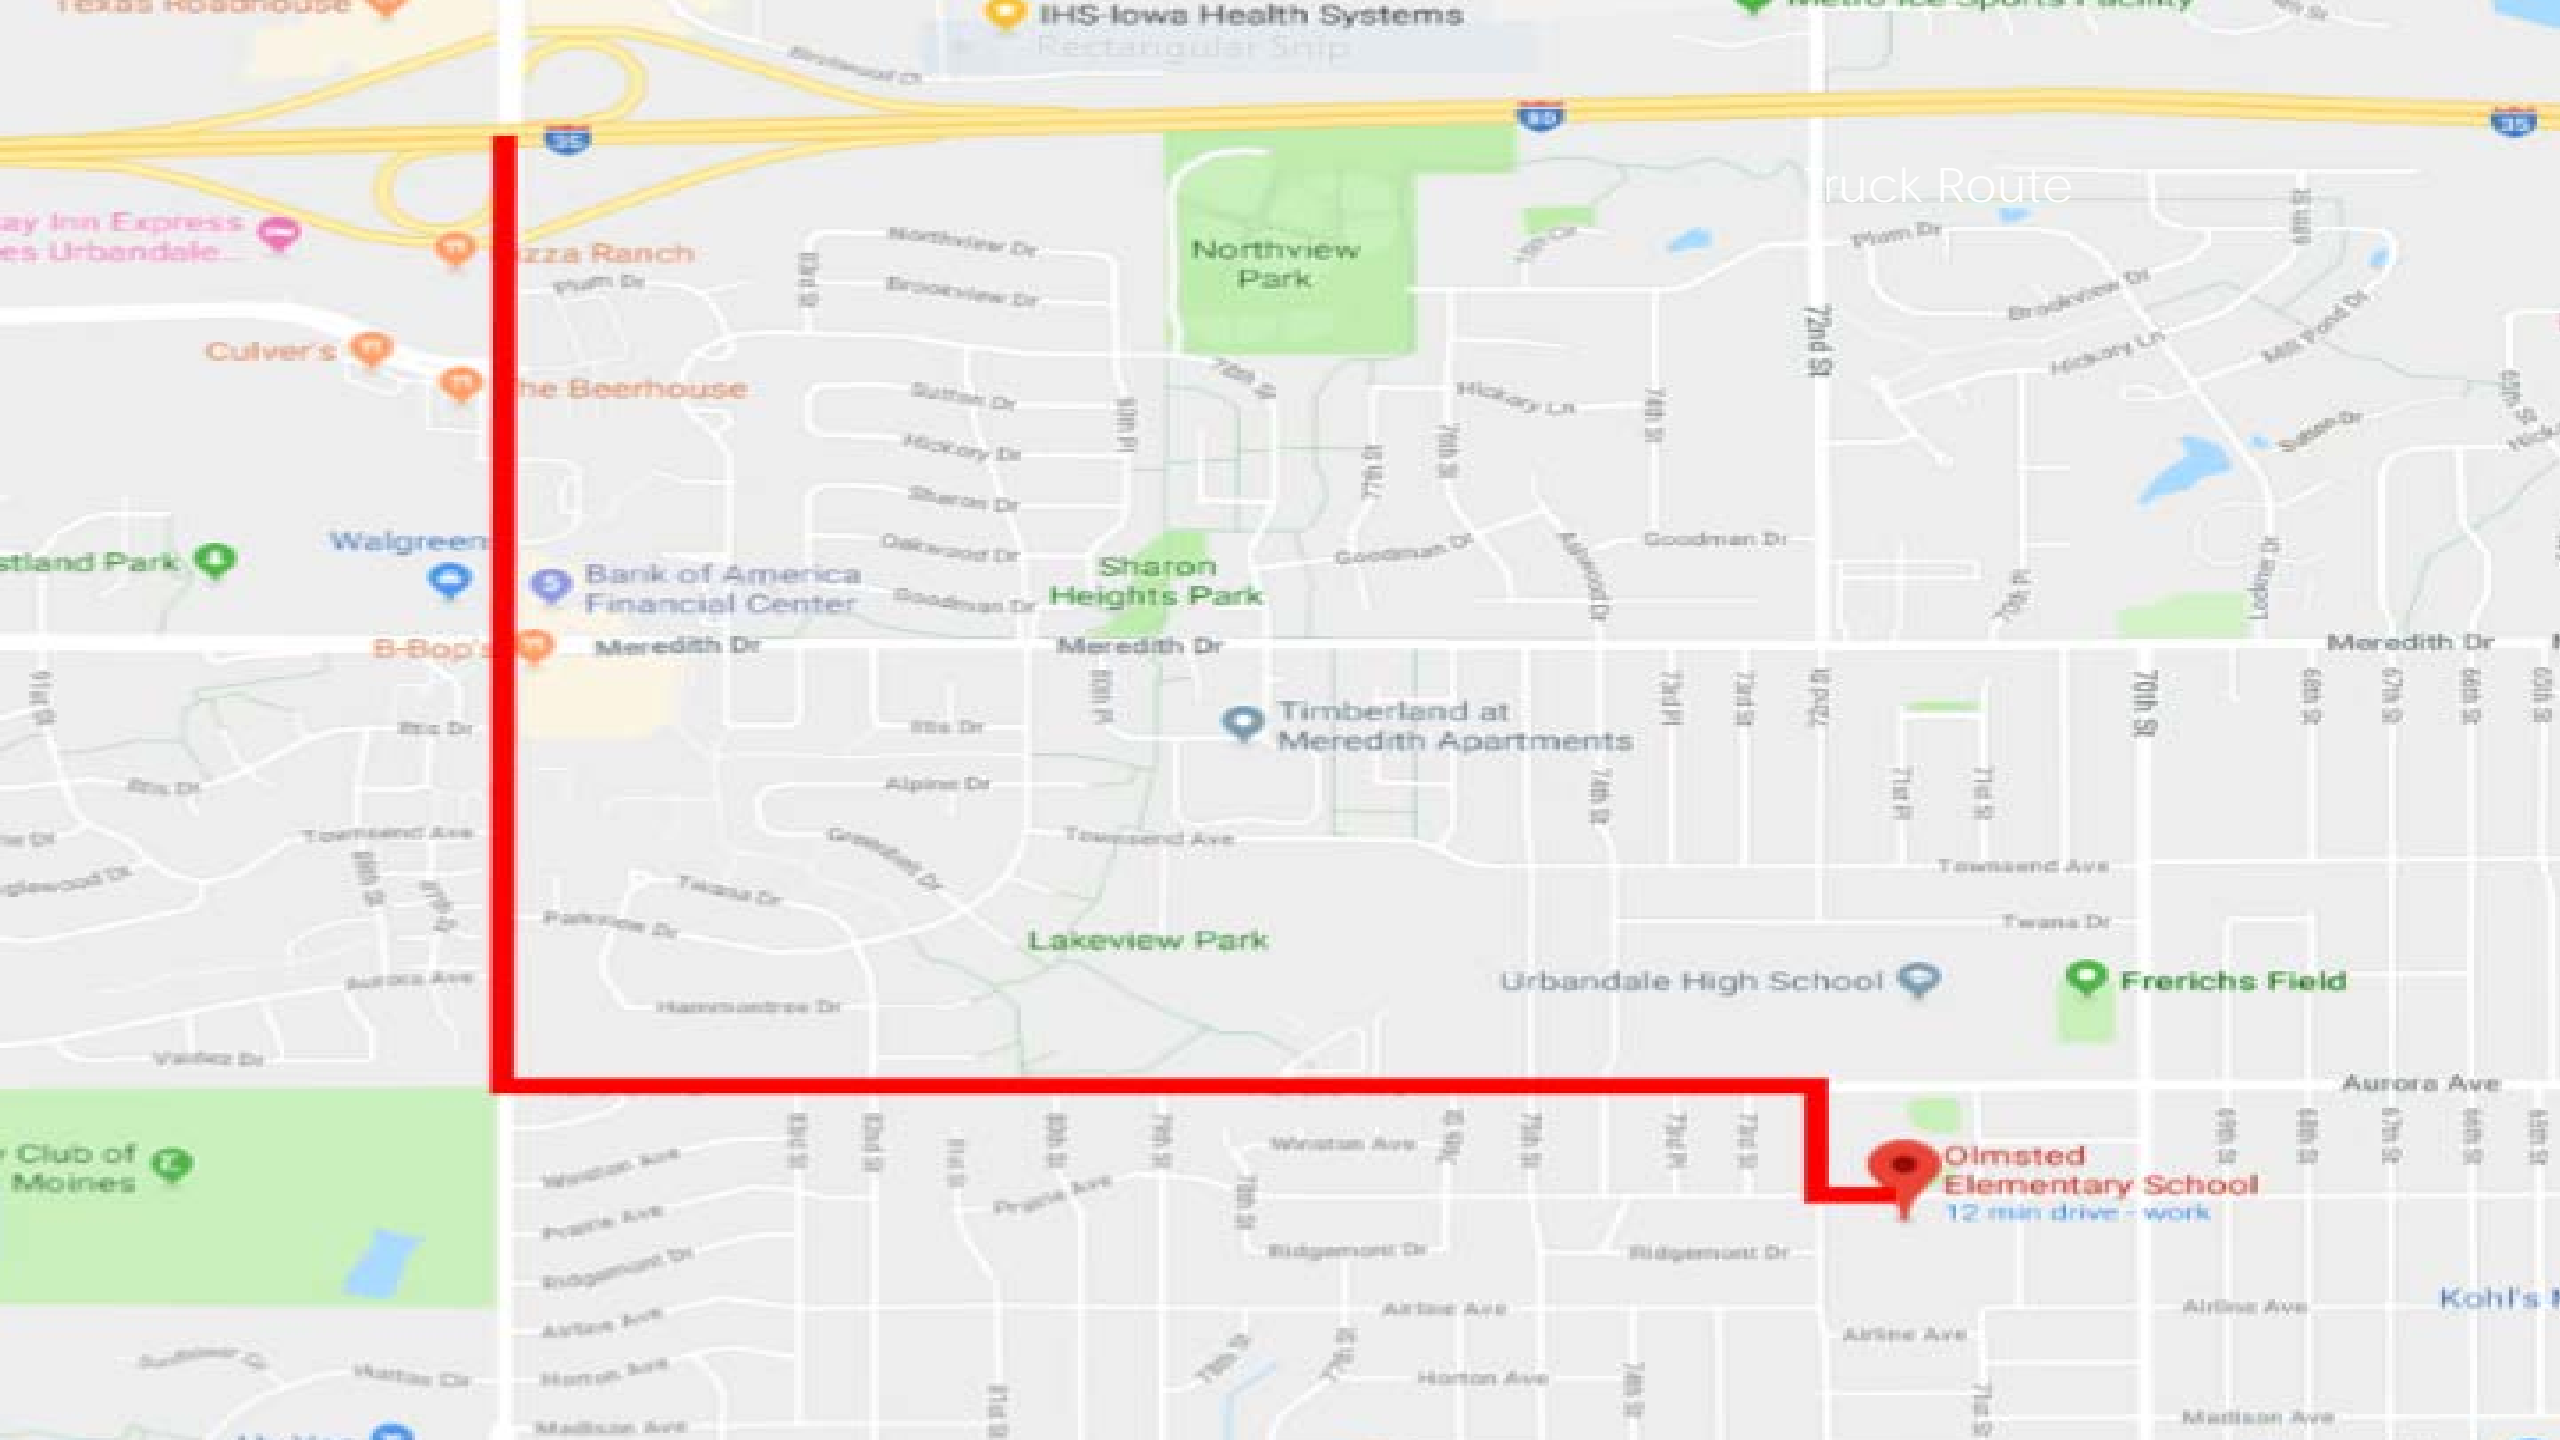

Truck Route

Olmsted Elementary School
12 min drive - work

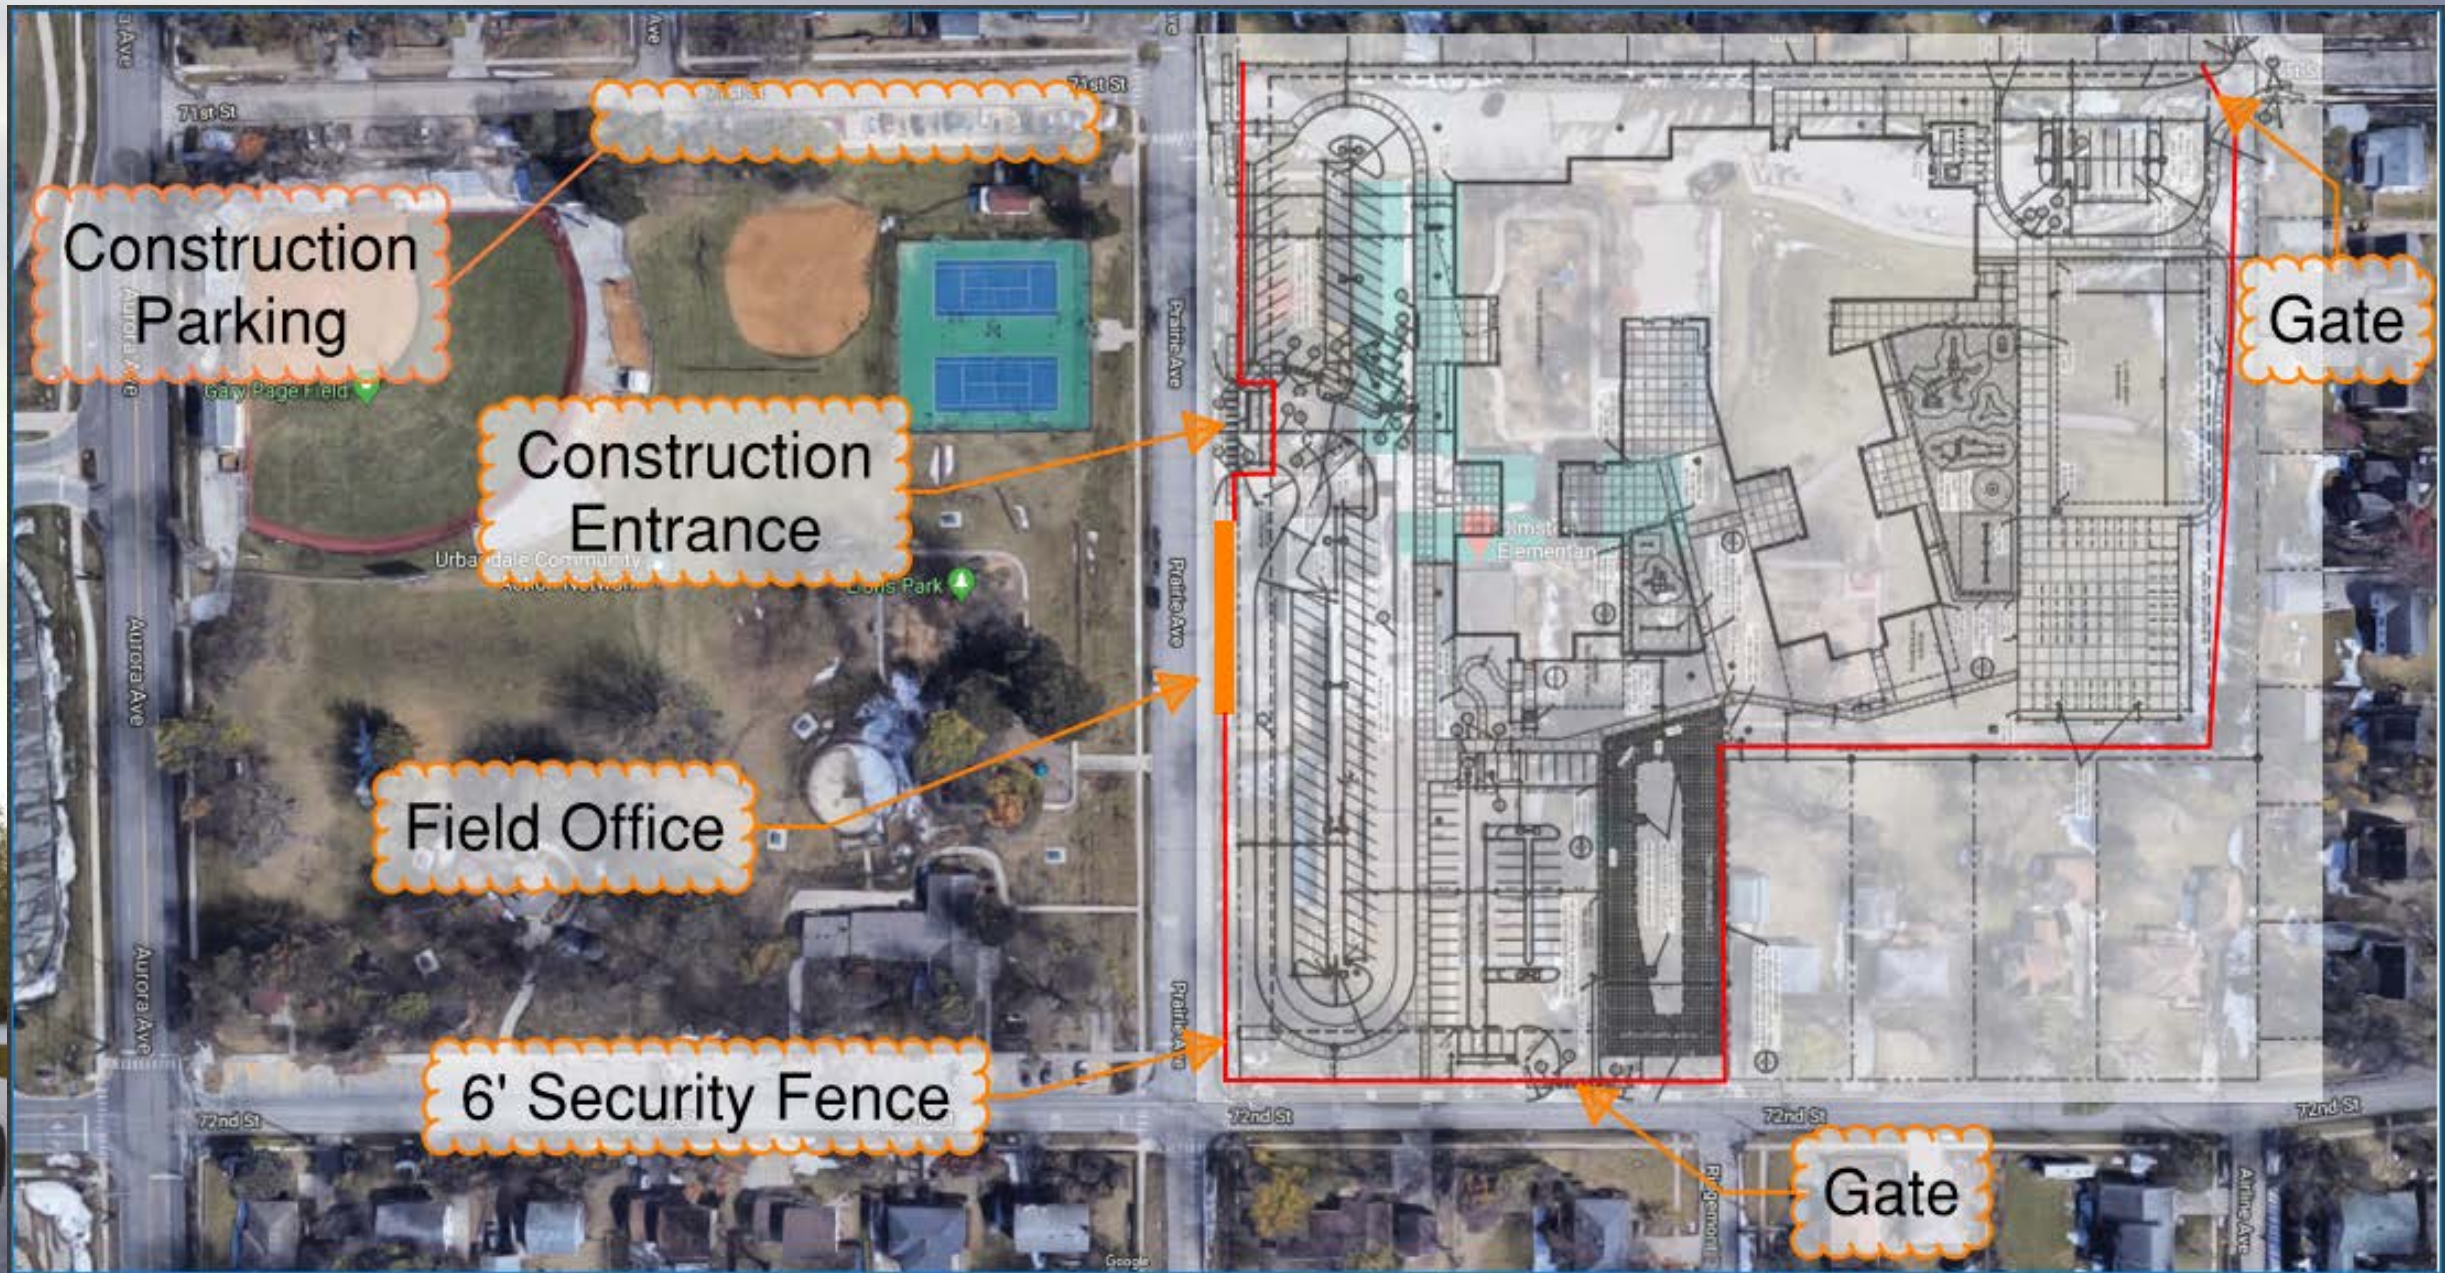

Construction
Parking

Construction
Entrance

Field Office

6' Security Fence

Gate

Gate

- Construction Timeline
- Demolition
- Traffic/ Sidewalk Impacts
- Site Layout
- Equipment
- Safety
- Hours of Operation



Questions?

